






File: WSU_HSB_Master Schedule Update, (Status Date 10-14-25) 2 of 22 Current Date: 10/14/25
 Status Date: 10/14/25

[illegible]

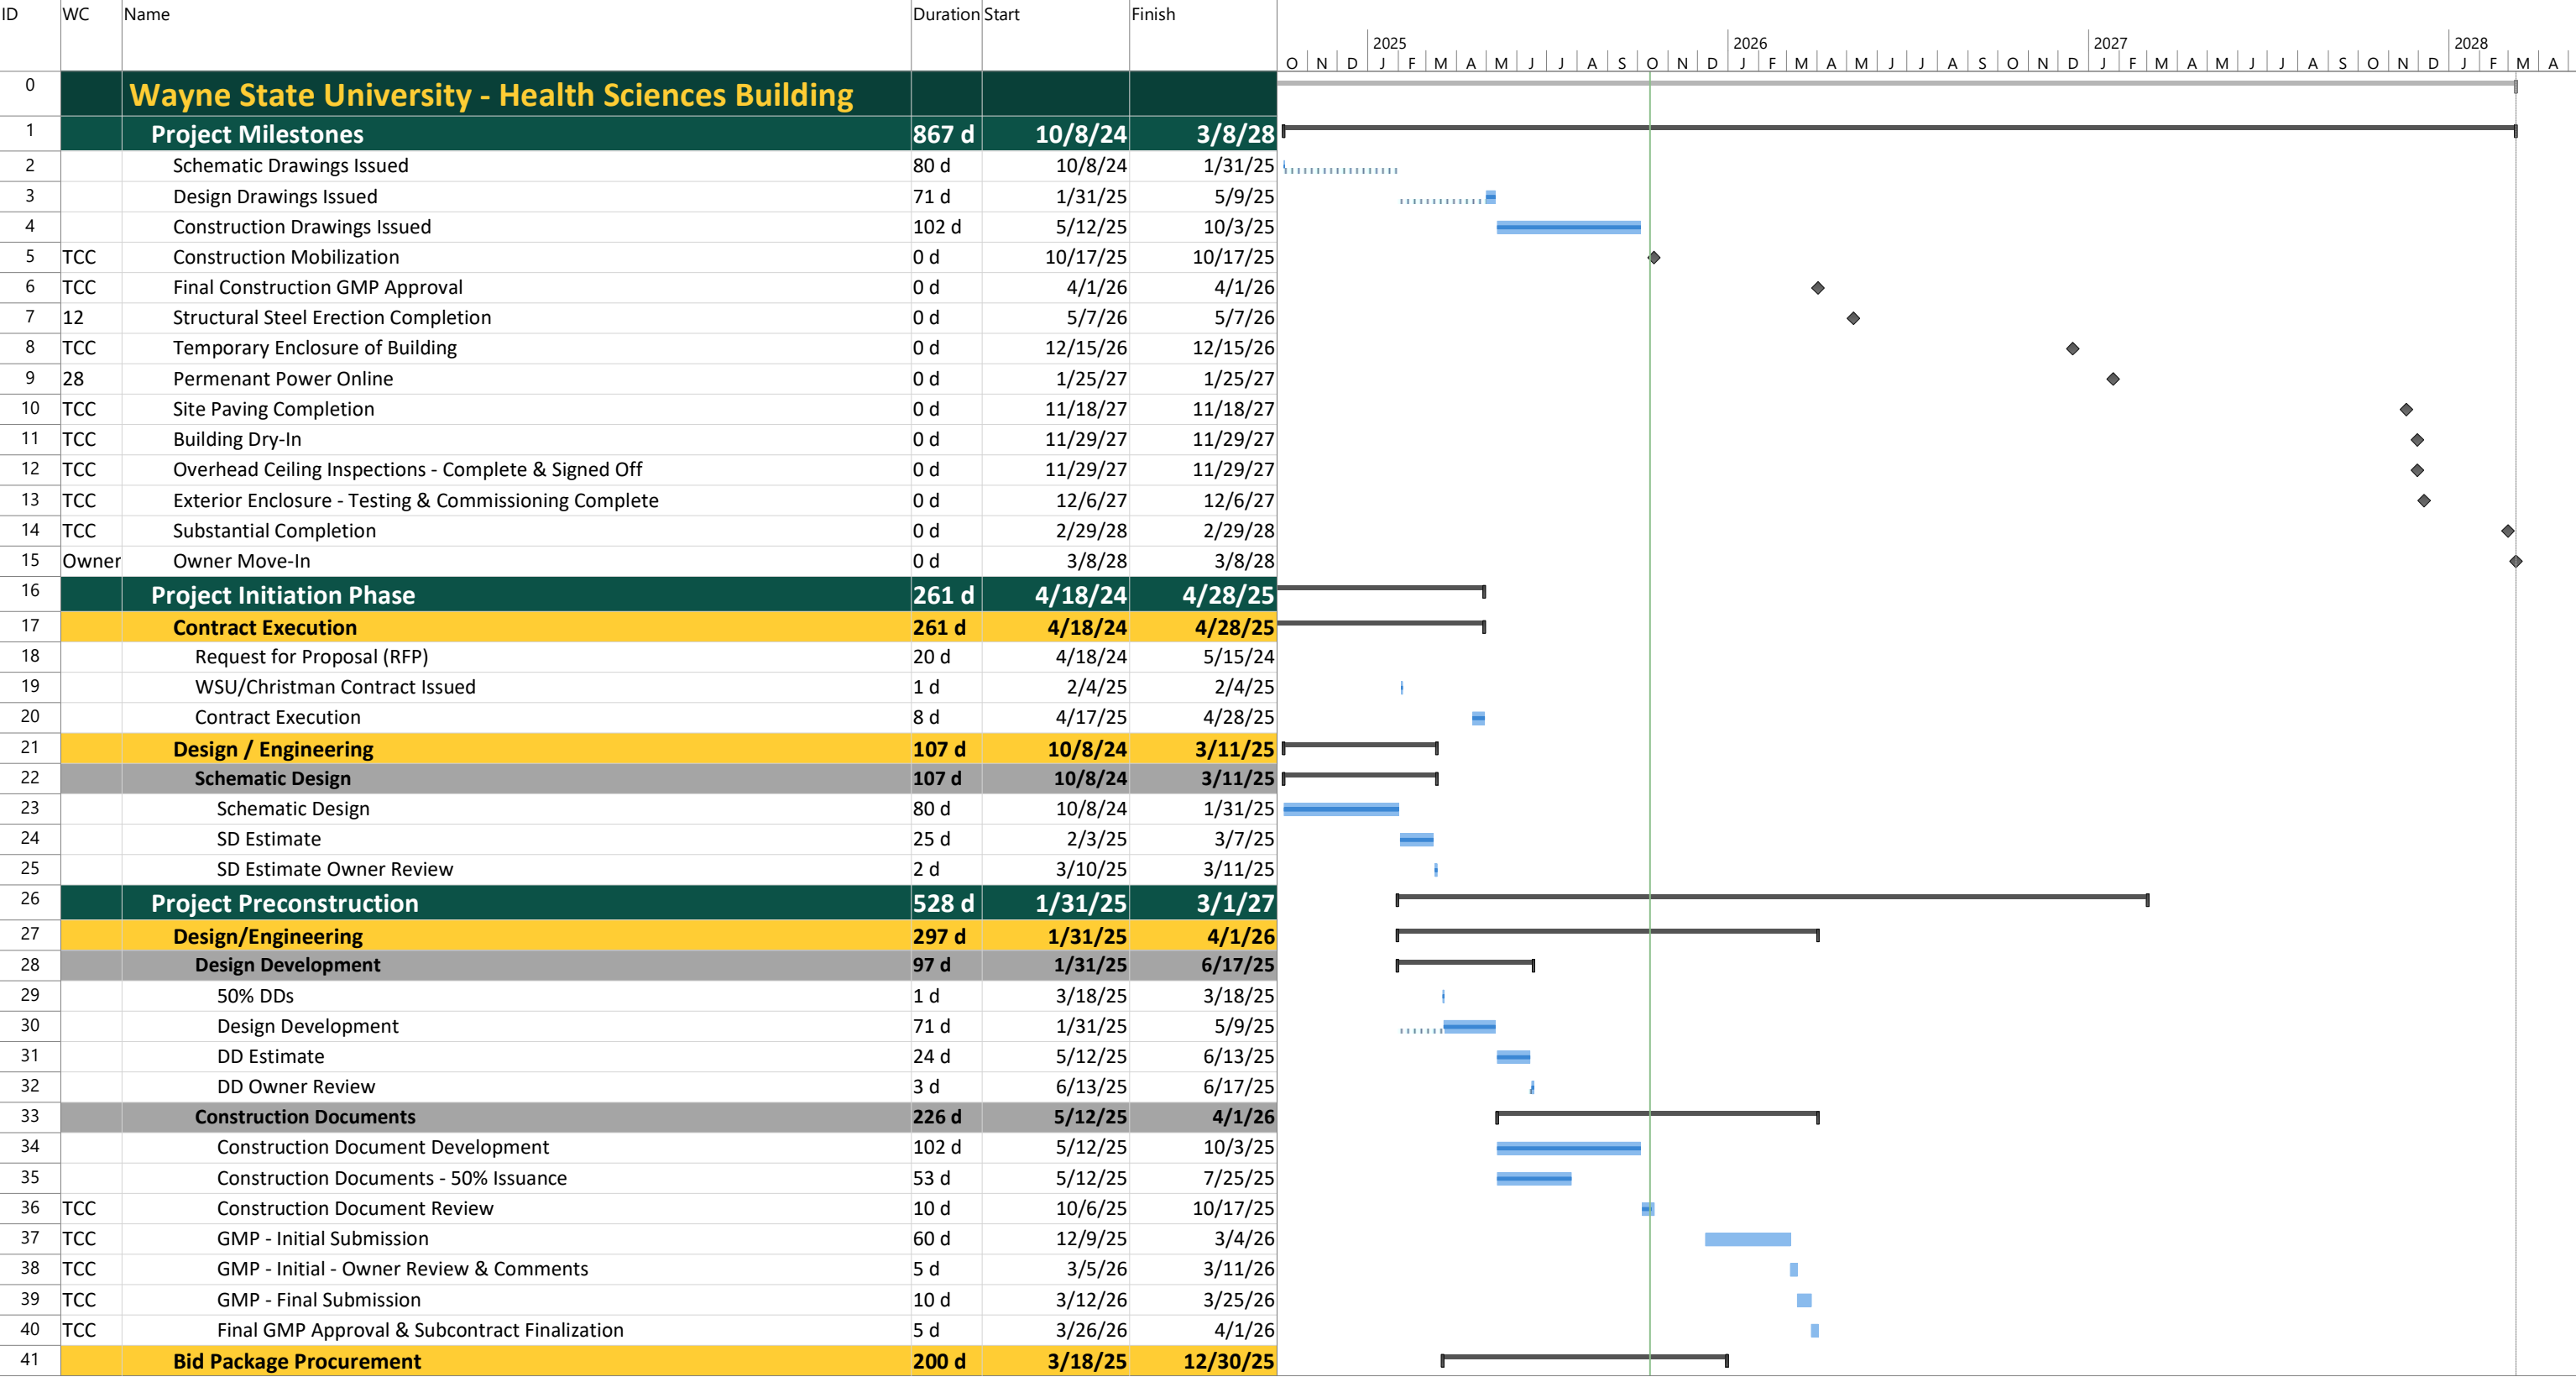

ID	WC	Name	Duration	Start	Finish	2025												2026												2027												2028			
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A									
127	28	ABB Busway	115 d	10/13/25	3/26/26																																								
128	28	ABB Busway - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
129	28	ABB Busway - Procurement	90 d	11/17/25	3/26/26																																								
130	28	ABB Power/Lighting Panels	75 d	10/13/25	1/29/26																																								
131	28	ABB Power/Lighting Panels - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
132	28	ABB Power/Lighting Panels - Procurement	50 d	11/17/25	1/29/26																																								
133	28	Lighting Sample Approvals	55 d	10/13/25	12/31/25																																								
134	28	Lighting Sample Approvals - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
135	28	Lighting Sample Approvals - Procurement	30 d	11/17/25	12/31/25																																								
136		Mechanical/Plumbing	235 d	10/13/25	9/15/26																																								
137	27	Air Handling Units	235 d	10/13/25	9/15/26																																								
138	27	Air Handling Units - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
139	27	Air Handling Units - Procurement	210 d	11/17/25	9/15/26																																								
140	27	Medical Vacuum System	205 d	10/13/25	8/3/26																																								
141	27	Medical Vacuum System - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
142	27	Medical Vacuum System - Procurement	180 d	11/17/25	8/3/26																																								
143	27	Specialty Clinical Sinks	175 d	10/13/25	6/19/26																																								
144	27	Specialty Clinical Sinks - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
145	27	Specialty Clinical Sinks - Procurement	150 d	11/17/25	6/19/26																																								
146	27	High Purity Deionized Water System & Generator	175 d	10/13/25	6/19/26																																								
147	27	High Purity Deionized Water System & Generator - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
148	27	High Purity Deionized Water System & Generator - Procurement	150 d	11/17/25	6/19/26																																								
149	27	Plumbing Fixtures	175 d	10/13/25	6/19/26																																								
150	27	Plumbing Fixtures - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
151	27	Plumbing Fixtures - Procurement	150 d	11/17/25	6/19/26																																								
152	27	Air Cooled Chillers	165 d	10/13/25	6/5/26																																								
153	27	Air Cooled Chillers - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
154	27	Air Cooled Chillers - Procurement	140 d	11/17/25	6/5/26																																								
155	27	Reverse Osmosis Generator & Reservoir	155 d	10/13/25	5/21/26																																								
156	27	Reverse Osmosis Generator & Reservoir - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
157	27	Reverse Osmosis Generator & Reservoir - Procurement	130 d	11/17/25	5/21/26																																								
158	27	Chilled Water Pumps	155 d	10/13/25	5/21/26																																								
159	27	Chilled Water Pumps - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
160	27	Chilled Water Pumps - Procurement	130 d	11/17/25	5/21/26																																								
161	27	Electric Humidifiers	150 d	10/13/25	5/14/26																																								
162	27	Electric Humidifiers - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
163	27	Electric Humidifiers - Procurement	125 d	11/17/25	5/14/26																																								
164	27	Air Compressor System	140 d	10/13/25	4/30/26																																								
165	27	Air Compressor System - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
166	27	Air Compressor System - Procurement	115 d	11/17/25	4/30/26																																								
167	27	Heating Hot Water Pumps	135 d	10/13/25	4/23/26																																								
168	27	Heating Hot Water Pumps - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
169	27	Heating Hot Water Pumps - Procurement	110 d	11/17/25	4/23/26																																								



ID	WC	Name	Duration	Start	Finish	2025												2026												2027												2028			
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A									
170	27	Exhaust Fans	125 d	10/13/25	4/9/26																																								
171	27	Exhaust Fans - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
172	27	Exhaust Fans - Procurement	100 d	11/17/25	4/9/26																																								
173	27	Gas Fired Boilers	125 d	10/13/25	4/9/26																																								
174	27	Gas Fired Boilers - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
175	27	Gas Fired Boilers - Procurement	100 d	11/17/25	4/9/26																																								
176	27	Nitrogen Generators	125 d	10/13/25	4/9/26																																								
177	27	Nitrogen Generators - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
178	27	Nitrogen Generators - Procurement	100 d	11/17/25	4/9/26																																								
179	27	Mechanical Roof Curbs	55 d	10/13/25	12/31/25																																								
180	27	Mechanical Roof Curbs - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
181	27	Mechanical Roof Curbs - Procurement	30 d	11/17/25	12/31/25																																								
182		Finishes	215 d	10/13/25	8/17/26																																								
183	TCC	Submittal Development & Approvals	30 d	11/25/25	1/9/26																																								
184	TCC	Sample Approvals	30 d	12/11/25	1/23/26																																								
185		Solid Core/Hollow Wood Doors	215 d	10/13/25	8/17/26																																								
186	20	Solid Core/Hollow Wood Doors - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
187	20	Solid Core/Hollow Wood Doors - Procurement	190 d	11/17/25	8/17/26																																								
188		Hollow Metal Doors and Frames	205 d	10/13/25	8/3/26																																								
189	20	Hollow Metal Doors and Frames - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
190	20	Hollow Metal Doors and Frames - Procurement	180 d	11/17/25	8/3/26																																								
191		Phenolic Lockers	190 d	10/13/25	7/13/26																																								
192	20	Phenolic Lockers - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
193	20	Phenolic Lockers - Procurement	165 d	11/17/25	7/13/26																																								
194		Precast Terrazzo Stair Treads	185 d	10/13/25	7/6/26																																								
195	22	Precast Terrazzo Stair Treads - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
196	22	Precast Terrazzo Stair Treads - Procurement	160 d	11/17/25	7/6/26																																								
197		Vertically Retractable Acoustic Partitions	175 d	10/13/25	6/19/26																																								
198	20	Vertically Retractable Acoustic Partitions - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
199	20	Vertically Retractable Acoustic Partitions - Procurement	150 d	11/17/25	6/19/26																																								
200		Integrated Interior Assemblies	160 d	10/13/25	5/29/26																																								
201	25	Integrated Interior Assemblies - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
202	25	Integrated Interior Assemblies - Procurement	135 d	11/17/25	5/29/26																																								
203		Laboratory Benches	155 d	10/13/25	5/21/26																																								
204	31	Laboratory Benches - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
205	31	Laboratory Benches - Procurement	130 d	11/17/25	5/21/26																																								
206		Snap-In Metal Pan Ceilings	135 d	10/13/25	4/23/26																																								
207	21	Snap-In Metal Pan Ceilings - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
208	21	Snap-In Metal Pan Ceilings - Procurement	110 d	11/17/25	4/23/26																																								
209		Lead Lined Walls	125 d	10/13/25	4/9/26																																								
210	20	Lead Lined Walls - Submittal Development & Approval	25 d	10/13/25	11/14/25																																								
211	20	Lead Lined Walls - Procurement	100 d	11/17/25	4/9/26																																								
212		Acoustical Panel Ceilings	105 d	10/13/25	3/12/26																																								



Wayne State University
Health Sciences Building
Proposal Schedule



ID	WC	Name	Duration	Start	Finish	2025							2026							2027							2028							
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F
213	21	Acoustical Panel Ceilings - Submittal Development & Approval	25 d	10/13/25	11/14/25																													
214	21	Acoustical Panel Ceilings - Procurement	80 d	11/17/25	3/12/26																													
215		Wood Looking LVT	105 d	10/13/25	3/12/26																													
216	23	Wood Looking LVT - Submittal Development & Approval	25 d	10/13/25	11/14/25																													
217	23	Wood Looking LVT - Procurement	80 d	11/17/25	3/12/26																													
218		Terrazzo Flooring	105 d	10/13/25	3/12/26																													
219	22	Terrazzo Flooring - Submittal Development & Approval	25 d	10/13/25	11/14/25																													
220	22	Terrazzo Flooring - Procurement	80 d	11/17/25	3/12/26																													
221		Porcelain Wall Tile	105 d	10/13/25	3/12/26																													
222	22	Porcelain Wall Tile - Submittal Development & Approval	25 d	10/13/25	11/14/25																													
223	22	Porcelain Wall Tile - Procurement	80 d	11/17/25	3/12/26																													
224		Interior Architectural Woodwork	95 d	10/13/25	2/26/26																													
225	20	Interior Architectural Woodwork - Submittal Development & Approval	25 d	10/13/25	11/14/25																													
226	20	Interior Architectural Woodwork - Procurement	70 d	11/17/25	2/26/26																													
227		Porcelain Floor Tile	85 d	10/13/25	2/12/26																													
228	23	Porcelain Floor Tile - Submittal Development & Approval	25 d	10/13/25	11/14/25																													
229	23	Porcelain Floor Tile - Procurement	60 d	11/17/25	2/12/26																													
230		Equipment	276 d	10/13/25	11/11/26																													
231		Loading Dock Equipment	255 d	10/13/25	10/13/26																													
232	20	Loading Dock Equipment - Submittal Development & Approval	25 d	10/13/25	11/14/25																													
233	20	Loading Dock Equipment - Procurement	230 d	11/17/25	10/13/26																													
234		Laboratory Equipment	215 d	1/12/26	11/11/26																													
235	31	Laboratory Equipment - Submittal Development & Approval	25 d	1/12/26	2/13/26																													
236	31	Laboratory Equipment - Procurement	190 d	2/16/26	11/11/26																													
237		Laboratory Casework	190 d	1/12/26	10/7/26																													
238	31	Laboratory Casework - Submittal Development & Approval	25 d	1/12/26	2/13/26																													
239	31	Laboratory Casework - Procurement	165 d	2/16/26	10/7/26																													
240		Environmental Cold Rooms	175 d	1/12/26	9/16/26																													
241	31	Environmental Cold Rooms - Submittal Development & Approval	25 d	1/12/26	2/13/26																													
242	31	Environmental Cold Rooms - Procurement	150 d	2/16/26	9/16/26																													
243		Laboratory Sterilizers - Glassware Washers and Dryers	155 d	1/12/26	8/18/26																													
244	31	Laboratory Sterilizers - Glassware Washers and Dryers - Submittal Development & Approval	25 d	1/12/26	2/13/26																													
245	31	Laboratory Sterilizers - Glassware Washers and Dryers - Procurement	130 d	2/16/26	8/18/26																													
246		Laboratory Fume Hoods	135 d	1/12/26	7/21/26																													
247	31	Laboratory Fume Hoods - Submittal Development & Approval	25 d	1/12/26	2/13/26																													
248	31	Laboratory Fume Hoods - Procurement	110 d	2/16/26	7/21/26																													
249		Biological Safety Cabinets - Procurement	115 d	1/12/26	6/22/26																													
250	31	Biological Safety Cabinets - Submittal Development & Approval	25 d	1/12/26	2/13/26																													
251	31	Biological Safety Cabinets - Procurement	90 d	2/16/26	6/22/26																													
252		Elevators	240 d	11/4/25	10/14/26																													
253	30	Submittal Development & Approvals	90 d	11/4/25	3/13/26																													
254	30	Service Elevator	150 d	3/16/26	10/14/26																													
255	30	Passenger Elevator(s)	100 d	3/16/26	8/4/26																													

File: WSU_HSB_Master Schedule Update, (Status Date 10-14-25) 7 of 22 Current Date: 10/14/25
 Status Date: 10/14/25

[illegible]



ID	WC	Name	Duration	Start	Finish	2025							2026							2027							2028							
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F
342		SW - Doestch Scoping/Cleanout of Existing Utilites & Structures	6 d	7/31/25	8/7/25																													
343		SW - Spalding DeDecker Existing Site Utility Survey	5 d	7/28/25	8/1/25																													
344		SW - Site Demolition	5 d	9/29/25	10/3/25																													
345	TCC	SW - Spalding DeDecker Civil Dwg. Set Revision - CD Update Based on Existing Con	10 d	10/3/25	10/16/25																													
346	02	SW - Cut, Cap, & Demo Existing Utilities	50 d	10/31/25	1/14/26																													
347	02	SW - Site Excavation/Grading	15 d	11/3/25	11/21/25																													
348	DTE	SW - DTE - Permenent Power Service	300 d	11/17/25	1/25/27																													
349	28	SW - Underground Electrical/Telecommunications Ductbanks	20 d	11/24/25	12/23/25																													
350	02	SW - Underground Storm Water	15 d	12/23/25	1/14/26																													
351	02	SW - Underground Sanitary Sewer	15 d	12/23/25	1/14/26																													
352	26	SW - Underground Fire Water	15 d	12/23/25	1/14/26																													
353	27	SW - Underground Gas	15 d	12/23/25	1/14/26																													
354	02	SW - Relocate Existing Manhole	10 d	1/13/26	1/26/26																													
355	05	SW - Traffic Control Setup - For Utility Taps	1 d	1/27/26	1/27/26																													
356	DTE	SW - Brush St. - Connect to Existing Gas (City of Det.)	5 d	1/28/26	2/3/26																													
357	02	SW - Brush St. - Connect to Existing Sewer (City of Det.)	5 d	1/28/26	2/3/26																													
358	02	SW - Brush St. - Connect to Existing Watermain (City of Det.)	5 d	1/28/26	2/3/26																													
359	02	SW - Chlorination Test	5 d	2/4/26	2/10/26																													
360	02	SW - Fire Hydrant Installed	5 d	2/4/26	2/10/26																													
361	02	SW - Fire Hydrant System Energized	5 d	2/11/26	2/17/26																													
362		Foundations & Concrete	125 d	11/24/25	5/21/26																													
363	02	FC - Earthwork & Aggregates - Building Pad Installation	20 d	11/24/25	12/23/25																													
364	10	FC - Elevator Pits - Elevator 1 & 2	20 d	12/3/25	12/31/25																													
365	10	FC - Elevator Pits - Service Elevator	20 d	12/3/25	12/31/25																													
366	10	FC - Undercutting for Foundations	10 d	12/3/25	12/16/25																													
367	10	FC - Foundations Excavation	15 d	12/24/25	1/15/26																													
368	27	FC - Underground MEP - SOG Sleeves & Penetrations	15 d	1/2/26	1/22/26																													
369	10	FC - Form, Rebar, Place - Foundations	10 d	1/16/26	1/29/26																													
370	10	FC - Form, Rebar, Place - Grade Beams	10 d	1/30/26	2/12/26																													
371	10	FC - Foundations - Anchorbolt Placement	10 d	1/30/26	2/12/26																													
372	10	FC - Slab-on-Grade - Prep	10 d	4/10/26	4/23/26																													
373	10	FC - Slab-on-Grade - Embeds	10 d	4/24/26	5/7/26																													
374	10	FC - Slab-on-Grade - Pour	10 d	5/8/26	5/21/26																													
375		Structural Steel & Decks	175 d	1/30/26	10/6/26																													
376		General	93 d	1/30/26	6/10/26																													
377	12	SSD - Structural Steel Crane Mobilization & Setup	5 d	1/30/26	2/5/26																													
378	12	SSD - Structural Steel Crane Demobilization	5 d	5/1/26	5/7/26																													
379	12	SSD - Erect Steel - Stair 1	10 d	5/22/26	6/5/26																													
380	12	SSD - Erect Steel - Stair 2	10 d	5/22/26	6/5/26																													
381	10	SSDS - Stair 1 - Concrete Infill	3 d	6/8/26	6/10/26																													
382	10	SSDS - Stair 2 - Concrete Infill	3 d	6/8/26	6/10/26																													
383		Steel Erection and Metal Decks	65 d	2/6/26	5/7/26																													
384		South Half	40 d	2/6/26	4/2/26																													



Wayne State University
Health Sciences Building
Proposal Schedule



ID	WC	Name	Duration	Start	Finish	2025												2026												2027												2028			
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A									
385		Steel Erection	30 d	2/6/26	3/19/26																																								
386	12	SSDS - Erect Steel - Ground Floor to Floor 2	5 d	2/6/26	2/12/26																																								
387	12	SSDS - Erect Steel - Floor 2 to Floor 3	5 d	2/13/26	2/19/26																																								
388	12	SSDS - Erect Steel - Floor 3 to Floor 4	5 d	2/20/26	2/26/26																																								
389	12	SSDS - Erect Steel - Floor 4 to Floor 5	5 d	2/27/26	3/5/26																																								
390	12	SSDS - Erect Steel - Floor 5 to Penthouse	5 d	3/6/26	3/12/26																																								
391	12	SSDS - Erect Steel - Penthouse to Roof	5 d	3/13/26	3/19/26																																								
392		Metal Decking	30 d	2/20/26	4/2/26																																								
393	12	SSDS - Metal Decking, Studs, Make Safe - Floor 2	5 d	2/20/26	2/26/26																																								
394	12	SSDS - Metal Decking, Studs, Make Safe - Floor 3	5 d	2/27/26	3/5/26																																								
395	12	SSDS - Metal Decking, Studs, Make Safe - Floor 4	5 d	3/6/26	3/12/26																																								
396	12	SSDS - Metal Decking, Studs, Make Safe - Floor 5	5 d	3/13/26	3/19/26																																								
397	12	SSDS - Metal Decking, Studs, Make Safe - Penthouse	5 d	3/20/26	3/26/26																																								
398	12	SSDS - Metal Decking - Roof	5 d	3/27/26	4/2/26																																								
399		North Half	35 d	3/20/26	5/7/26																																								
400		Erect Steel	30 d	3/20/26	4/30/26																																								
401	12	SSDN - Erect Steel - Ground Floor to Floor 2	5 d	3/20/26	3/26/26																																								
402	12	SSDN - Erect Steel - Floor 2 to Floor 3	5 d	3/27/26	4/2/26																																								
403	12	SSDN - Erect Steel - Floor 3 to Floor 4	5 d	4/3/26	4/9/26																																								
404	12	SSDN - Erect Steel - Floor 4 to Floor 5	5 d	4/10/26	4/16/26																																								
405	12	SSDN - Erect Steel - Floor 5 to Penthouse	5 d	4/17/26	4/23/26																																								
406	12	SSDN - Erect Steel - Penthouse to Roof	5 d	4/24/26	4/30/26																																								
407		Metal Decking	25 d	4/3/26	5/7/26																																								
408	12	SSDN - Metal Decking, Studs, Make Safe - Floor 2	5 d	4/3/26	4/9/26																																								
409	12	SSDN - Metal Decking, Studs, Make Safe - Floor 3	5 d	4/10/26	4/16/26																																								
410	12	SSDN - Metal Decking, Studs, Make Safe - Floor 4	5 d	4/17/26	4/23/26																																								
411	12	SSDN - Metal Decking, Studs, Make Safe - Floor 5	5 d	4/17/26	4/23/26																																								
412	12	SSDN - Metal Decking, Studs, Make Safe - Penthouse	5 d	4/24/26	4/30/26																																								
413	12	SSDN - Metal Decking - Roof	5 d	5/1/26	5/7/26																																								
414		Slab Prep and Slab On Deck	135 d	3/27/26	10/6/26																																								
415		South Half	70 d	3/27/26	7/6/26																																								
416		Slab On Deck Prep	50 d	3/27/26	6/5/26																																								
417	MEPF	SSDS - MEPF - Inserts For Floor Below - Penthouse Pour	10 d	3/27/26	4/9/26																																								
418	MEPF	SSDS - MEPF - Inserts For Floor Below - Level 5 Pour	10 d	4/10/26	4/23/26																																								
419	MEPF	SSDS - MEPF - Inserts For Floor Below - Level 4 Pour	10 d	4/24/26	5/7/26																																								
420	MEPF	SSDS - MEPF - Inserts For Floor Below - Level 3 Pour	10 d	5/8/26	5/21/26																																								
421	MEPF	SSDS - MEPF - Inserts For Floor Below - Level 2 Pour	10 d	5/22/26	6/5/26																																								
422		Slab On Deck	65 d	4/3/26	7/6/26																																								
423	10	SSDS - Slab-on-Deck - Roof	10 d	4/3/26	4/16/26																																								
424	10	SSDS - Concrete Curbs - Penthouse	5 d	4/17/26	4/23/26																																								
425	10	SSDS - Slab-on-Deck - Penthouse	10 d	4/24/26	5/7/26																																								
426	10	SSDS - Slab-on-Deck - Floor 5	10 d	5/8/26	5/21/26																																								
427	10	SSDS - Slab-on-Deck - Floor 4	10 d	5/22/26	6/5/26																																								



ID	WC	Name	Duration	Start	Finish																								
						O	N	D	2025							2026							2027						
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
428	10	SSDS - Slab-on-Deck - Floor 3	10 d	6/8/26	6/19/26																								
429	10	SSDS - Slab-on-Deck - Floor 2	10 d	6/22/26	7/6/26																								
430		North Half	85 d	6/8/26	10/6/26																								
431		Slab On Deck Prep	50 d	6/8/26	8/17/26																								
432	MEPF	SSDN - MEPF - Inserts For Floor Below - Penthouse Pour	10 d	6/8/26	6/19/26																								
433	MEPF	SSDN - MEPF - Inserts For Floor Below - Level 5 Pour	10 d	6/22/26	7/6/26																								
434	MEPF	SSDN - MEPF - Inserts For Floor Below - Level 4 Pour	10 d	7/7/26	7/20/26																								
435	MEPF	SSDN - MEPF - Inserts For Floor Below - Level 3 Pour	10 d	7/21/26	8/3/26																								
436	MEPF	SSDN - MEPF - Inserts For Floor Below - Level 2 Pour	10 d	8/4/26	8/17/26																								
437		Slab On Deck	65 d	7/7/26	10/6/26																								
438	10	SSDN - Slab-on-Deck - Roof	10 d	7/7/26	7/20/26																								
439	10	SSDN - Concrete Curbs - Penthouse	5 d	7/21/26	7/27/26																								
440	10	SSDN - Slab-on-Deck - Penthouse	10 d	7/28/26	8/10/26																								
441	10	SSDN - Slab-on-Deck - Floor 5	10 d	8/11/26	8/24/26																								
442	10	SSDN - Slab-on-Deck - Floor 4	10 d	8/25/26	9/8/26																								
443	10	SSDN - Slab-on-Deck - Floor 3	10 d	9/9/26	9/22/26																								
444	10	SSDN - Slab-on-Deck - Floor 2	10 d	9/23/26	10/6/26																								
445		Building Enclosure	1004 d	1/2/24	12/13/27																								
446		General	377 d	6/11/26	12/6/27																								
447	18	EG - Exterior Framing	30 d	6/11/26	7/23/26																								
448	12/18	EG - Vapor Barrier/Waterproofing	30 d	7/24/26	9/3/26																								
449	18	EG - Z-Furring Strips & Insulation	20 d	9/4/26	10/2/26																								
450	18	EG - Gypsum Sheathing	15 d	10/5/26	10/23/26																								
451	TCC	EG - Temporary Enclosure (If Required)	30 d	11/2/26	12/15/26																								
452	18	EG - Solar Shade Devices	20 d	9/17/27	10/14/27																								
453	TCC	EG - Exterior Envelope - Testing & Commissioning	5 d	11/30/27	12/6/27																								
454		Penthouse	285 d	5/1/26	6/15/27																								
455	12	EP - Precast Support Steel	20 d	5/1/26	5/29/26																								
456	09	EP - Precast Concrete - Double Sided Sandwich Panels	60 d	3/2/27	5/24/27																								
457	18	EP - Louvers	10 d	5/25/27	6/8/27																								
458	14	EP - Aluminum Coping	5 d	6/9/27	6/15/27																								
459	TCC	EP - Penthouse Enclosure Complete	0 d	6/15/27	6/15/27																								
460		Roof	40 d	8/11/26	10/6/26																								
461	18	ER - Metal Screenwall - Framing	10 d	8/11/26	8/24/26																								
462	18	ER - Metal Screenwall - Panels	20 d	8/25/26	9/22/26																								
463	14	ER - Aluminum Coping	5 d	9/23/26	9/29/26																								
464	14	ER - Scupper/Flashings	5 d	9/30/26	10/6/26																								
465	TCC	ER - Roof Enclosure Complete	0 d	10/6/26	10/6/26																								
466		North	944 d	1/2/24	9/16/27																								
467	18	EN - Metal Wall Exterior Panels (Grits, Clips, Insulation)	20 d	1/2/24	1/29/24																								
468	11	EN - Limestone Water Table	10 d	9/4/26	9/18/26																								
469	18	EN - Curtainwall - Unitized System (Survey, Layout & Install Anchors)	10 d	10/14/26	10/27/26																								
470	18	EN - Layout & Install Anchors	5 d	10/14/26	10/20/26																								



File: WSU_HSB_Master Schedule Update, (Status Date 10-14-25) 12 of 22 Current Date: 10/14/25
 Status Date: 10/14/25



ID	WC	Name	Duration	Start	Finish																								
						O	N	D	2025							2026							2027						
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
514	18	ES - Curtainwall - Unitized System - Horizontal and Vertical Sunshades	10 d	8/5/27	8/18/27																								
515	18	ES - Metal Wall Exterior Panels	20 d	10/8/27	11/4/27																								
516	TCC	ES - WSU Exterior Signage	5 d	12/7/27	12/13/27																								
517	TCC	ES - South Elevation Complete	0 d	12/13/27	12/13/27																								
518		West	939 d	3/19/24	11/29/27																								
519	18	EW - Metal Wall Exterior Panels (Grits, Clips, Insulation)	15 d	3/19/24	4/8/24																								
520	11	EW - Limestone Water Table	10 d	9/4/26	9/18/26																								
521	18	EW - Stick Built - Layout & Install Anchors	5 d	10/28/26	11/3/26																								
522	18	EW - Curtainwall - Unitized System (Survey, Layout & Install Anchors)	5 d	11/11/26	11/17/26																								
523	18	EW - Stick-Built Curtainwall - 1st Floor (Framing - Verticals and Horizontals)	10 d	12/4/26	12/17/26																								
524	18	EW - Stick-Built Curtainwall - 1st Floor (Prep Framing & Install Glass)	10 d	12/18/26	1/4/27																								
525	18	EW - Stick-Built Curtainwall - 1st Floor (Install Covers & Weatherseal)	10 d	1/5/27	1/18/27																								
526	09	EW - Precast Concrete Exterior Panels	60 d	3/2/27	5/24/27																								
527	18	EW - Curtainwall - Unitized System	10 d	8/5/27	8/18/27																								
528	18	EW - Curtainwall - Unitized System - Horizontal and Vertical Sunshades	10 d	8/19/27	9/1/27																								
529	18	EW - Metal Wall Exterior Panels	15 d	11/5/27	11/29/27																								
530	TCC	EW - West Elevation Complete	0 d	11/29/27	11/29/27																								
531		Elliman Connector	130 d	3/2/27	9/1/27																								
532	09	EEC - Precast Concrete Exterior Panels	60 d	3/2/27	5/24/27																								
533	18	EEC - Exterior Glazing	60 d	5/25/27	8/18/27																								
534	14	EEC - Aluminum Coping	5 d	8/19/27	8/25/27																								
535	14	EEC - Sill/Metal Flashings	5 d	8/26/27	9/1/27																								
536	TCC	EEC - Elliman Connector Envelope Complete	0 d	9/1/27	9/1/27																								
537		Scott Hall Bridge	4 d	5/25/27	5/28/27																								
538	18	ESHB - Curtainwall	2 d	5/25/27	5/26/27																								
539	20	ESHB - Metal Wood Soffit - Longboard	2 d	5/27/27	5/28/27																								
540	TCC	ESHB - WSU Exterior Signage	2 d	5/27/27	5/28/27																								
541	TCC	ESHB - Scott Hall Bridge Enclosure Complete	0 d	5/28/27	5/28/27																								
542		Roofing	140 d	5/1/26	11/17/26																								
543		Roof (Level 5)	140 d	5/1/26	11/17/26																								
544	27	R5 - Roof Drains	5 d	5/1/26	5/7/26																								
545	12	R5 - Roof to Penthouse Stair (Level 5 to Level 6)	5 d	5/1/26	5/7/26																								
546	14	R5 - Roofing Phase #1 - Densdeck and Vapor Barrier	25 d	7/21/26	8/24/26																								
547	20	R5 - Woodblocking, Plywood Nailers	5 d	8/25/26	8/31/26																								
548	14	R5 - Roofing Phase #2 - PVC Roof	25 d	9/1/26	10/6/26																								
549	14	R5 - Roof/Pad Flashings & Trim	15 d	10/7/26	10/27/26																								
550	14	R5 - Roofing Walk Pads	5 d	10/28/26	11/3/26																								
551	28	R5 - Lightning Protection	10 d	11/4/26	11/17/26																								
552	TCC	RS - Roof Level 5 Complete	0 d	11/17/26	11/17/26																								
553		Penthouse (Level 6)	135 d	5/8/26	11/17/26																								
554	10	RP6 - Equipment Curbs & Rails	10 d	5/8/26	5/21/26																								
555	27	RP6 - Roof Drains	5 d	5/8/26	5/14/26																								
556	14	RP6 - Roofing Phase #1 - Densdeck and Vapor Barrier	25 d	7/21/26	8/24/26																								



ID	WC	Name	Duration	Start	Finish	2025												2026												2027												2028			
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A									
557	20	RP6 - Woodblocking, Plywood Nailers	5 d	8/25/26	8/31/26																																								
558	14	RP6 - Roofing Phase #2 - PVC Roof	25 d	9/1/26	10/6/26																																								
559	14	RP6 - Roof/Pad Flashings & Trim	15 d	10/7/26	10/27/26																																								
560	14	RP6 - Roofing Walk Pads	5 d	10/28/26	11/3/26																																								
561	28	RP6 - Lightning Protection	10 d	11/4/26	11/17/26																																								
562	TCC	RP6 - Penthouse Level 6 Complete	0 d	11/17/26	11/17/26																																								
563		High Roof (Level 7)	135 d	5/8/26	11/17/26																																								
564	12	R7 - Elevator Machine Room Stair	5 d	5/8/26	5/14/26																																								
565	27	R7 - Roof Drains	5 d	5/8/26	5/14/26																																								
566	14	R7 - Roofing Phase #1 - Densdeck and Vapor Barrier	25 d	7/21/26	8/24/26																																								
567	20	R7 - Woodblocking, Plywood Nailers	5 d	8/25/26	8/31/26																																								
568	14	R7 - Roofing Phase #2 - PVC Roof	25 d	9/1/26	10/6/26																																								
569	14	R7 - Roof/Pad Flashings & Trim	15 d	10/7/26	10/27/26																																								
570	28	R7 - Lightning Protection	10 d	11/4/26	11/17/26																																								
571	TCC	R7 - High Roof Level 7 Complete	0 d	11/17/26	11/17/26																																								
572		Building Interiors	540 d	11/3/25	12/20/27																																								
573		Scott Hall Bridge	465 d	11/3/25	9/1/27																																								
574	12	SHB - Pre-Fabricate & Assemble Bridge	60 d	11/3/25	1/29/26																																								
575	10	SHB - Drive Piles/Supports for Bridge Trusses	5 d	1/9/26	1/15/26																																								
576	10	SHB - Underground Piers - Set Cages/Concrete	10 d	1/16/26	1/29/26																																								
577	10	SHB - Set Anchorbolts	5 d	1/30/26	2/5/26																																								
578	10	SHB - Form, Rebar, Place - Concrete Walls/Bases	5 d	2/6/26	2/12/26																																								
579	12	SHB - Set Bridge/Connector	5 d	4/3/26	4/9/26																																								
580	TCC	SHB - Interior Barricades	5 d	6/2/27	6/8/27																																								
581	MEPF	SHB - Cut, Cap & Make Safe - Any MEPF Systems	5 d	6/9/27	6/15/27																																								
582	20	SHB - Interior Demolition - Expose to Exterior Structure	10 d	6/16/27	6/29/27																																								
583	09	SHB - Remove Existing Exterior Precast Panels	15 d	6/30/27	7/21/27																																								
584	12	SHB - Install Any Supplemental Temporary Steel to Shore Up Existing Exterior	10 d	7/22/27	8/4/27																																								
585	21	SHB - Frame Out New Bridge Entrance in Scott Hall Exterior	20 d	8/5/27	9/1/27																																								
586	TCC	SHB - Scott Hall Bridge Interior Complete	0 d	9/1/27	9/1/27																																								
587		Elliman Connector	466 d	1/15/26	11/11/27																																								
588	TCC	EC - Interior Barricades/Secure Perimeter of Elliman	5 d	1/15/26	1/21/26																																								
589	TCC	EC - Decommissioning of Existing Loading Dock & Door	3 d	1/22/26	1/26/26																																								
590	MEPF	EC - Cut, Cap, & Make Safe - Loading Dock Door and Exterior	3 d	1/27/26	1/29/26																																								
591	02	EC - Demolition of Existing Concrete Paving/Drive	5 d	1/30/26	2/5/26																																								
592	02	EC - Demolition of Existing Side Walls	2 d	1/30/26	2/2/26																																								
593	02	EC - Excavation and Grading	10 d	2/6/26	2/19/26																																								
594	27	EC - Underground MEP	15 d	2/20/26	3/12/26																																								
595	10	EC - Foundations	10 d	2/20/26	3/5/26																																								
596	10	EC - Concrete - Built-Up Slab on Foam	10 d	3/6/26	3/19/26																																								
597	10	EC - Foundations - Set Anchorbolts	5 d	3/6/26	3/12/26																													</											



ID	WC	Name	Duration	Start	Finish																								
						2025												2026											
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S
600	10	EC - SOG Prep & Place	15 d	4/10/26	4/30/26																								
601	10	EC - SOG - Embeds	3 d	4/10/26	4/14/26																								
602	18	EC - Exterior Enclosure	50 d	5/1/26	7/13/26																								
603	14	EC - Roofing	20 d	9/23/26	10/20/26																								
604	MEPF	EC - Overhead MEPF	60 d	10/21/26	1/18/27																								
605	21	EC - Interior Walls	10 d	10/21/26	11/3/26																								
606	MEPF	EC - In-Wall MEPF	40 d	11/4/26	1/4/27																								
607	MEPF	EC - In-Wall MEPF Inspection	5 d	1/5/27	1/11/27																								
608	21	EC - Close-In Walls	10 d	1/12/27	1/25/27																								
609	20B	EC - Spray Fireproofing	15 d	1/19/27	2/8/27																								
610	21	EC - Door Frame Installation	20 d	2/9/27	3/8/27																								
611	20	EC - Loading Dock Overhead Coiling Doors/Dock Levelers Installation	20 d	3/9/27	4/5/27																								
612	21	EC - Hang, Tape & Finish Drywall	10 d	4/6/27	4/19/27																								
613	21	EC - Ceiling Grid/Frame Installation	35 d	4/20/27	6/8/27																								
614	23	EC - Flooring	30 d	4/20/27	6/1/27																								
615	24	EC - Prime/Paint First Coat	20 d	4/20/27	5/17/27																								
616	20	EC - Door Hardware	20 d	5/18/27	6/15/27																								
617	28	EC - Light Fixtures	40 d	6/9/27	8/4/27																								
618	27	EC - Grilles/Diffusers	15 d	6/9/27	6/29/27																								
619	MEPF	EC - Overhead MEPF Inspection	5 d	8/5/27	8/11/27																								
620	21	EC - Ceiling Tile Installation	15 d	8/12/27	9/1/27																								
621	24	EC - Finish Paint - 2nd Coat	20 d	9/2/27	9/30/27																								
622	MEPF	EC - MEPF Finish Devices	30 d	10/1/27	11/11/27																								
623	TCC	EC - Elliman Connector Interior Complete	0 d	11/11/27	11/11/27																								
624		Main Building	435 d	4/3/26	12/20/27																								
625		Building Services	273 d	4/3/26	4/29/27																								
626		Passenger Elevators	252 d	4/3/26	3/31/27																								
627	27	PE - Elevator Pit Sumps	15 d	4/3/26	4/23/26																								
628	26	PE - Fire Suppression	5 d	4/24/26	4/30/26																								
629	28	PE - Fire Alarm	5 d	4/24/26	4/30/26																								
630	12	PE - Elevator Hoist Beams & Divider Beams	20 d	5/1/26	5/29/26																								
631	12	PE - Elevator Miscellaneous Steel	10 d	6/1/26	6/12/26																								
632	20	PE - Shaft Platform	5 d	6/15/26	6/19/26																								
633	12	PE - Weld Plate	5 d	6/15/26	6/19/26																								
634	30	PE - Elevator Install	90 d	8/5/26	12/11/26																								
635	28	PE - Elevators - Connect to Permenent Power	5 d	1/26/27	2/1/27																								
636	30	PE - Elevator Cab Finishes	30 d	2/2/27	3/15/27																								
637	30	PE - Elevator Card Reader/Access Control	10 d	2/2/27	2/15/27																								
638	30	PE - Elevator - Initial Inspection	1 d	3/16/27	3/16/27																								
639	30	PE - Elevator Cars - Final Adjusting	5 d	3/23/27	3/29/27																								
640	30	PE - Elevator Cars - Final Cleaning	1 d	3/30/27	3/30/27																								
641	30	PE - Elevator - Commissioning & Final Inspection	1 d	3/31/27	3/31/27																								
642	30	PE - Passenger Elevators Complete	0 d	3/31/27	3/31/27																								



ID	WC	Name	Duration	Start	Finish	2025												2026												2027												2028											
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A																	
643		Service Elevator	273 d	4/3/26	4/29/27																																																
644	27	SE - Elevator Pit Sumps	15 d	4/3/26	4/23/26																																																
645	26	SE - Fire Suppression	5 d	4/24/26	4/30/26																																																
646	28	SE - Fire Alarm	5 d	4/24/26	4/30/26																																																
647	12	SE - Elevator Hoist Beams & Divider Beams	20 d	5/1/26	5/29/26																																																
648	12	SE - Elevator Miscellaneous Steel	10 d	6/1/26	6/12/26																																																
649	20	SE - Shaft Platform	5 d	6/15/26	6/19/26																																																
650	12	SE - Weld Plate	5 d	6/15/26	6/19/26																																																
651	30	SE - Elevator Install	90 d	10/15/26	2/23/27																																																
652	28	SE - Elevators - Connect to Permenent Power	5 d	2/24/27	3/2/27																																																
653	30	SE - Elevator Cab Finishes	30 d	3/3/27	4/13/27																																																
654	30	SE - Elevator Card Reader/Access Control	10 d	3/3/27	3/16/27																																																
655	30	SE - Elevator - Initial Inspection	1 d	4/14/27	4/14/27																																																
656	30	SE - Elevator Cars - Final Adjusting	5 d	4/21/27	4/27/27																																																
657	30	SE - Elevator Cars - Final Cleaning	1 d	4/28/27	4/28/27																																																
658	30	SE - Elevator - Commissioning & Final Inspection	1 d	4/29/27	4/29/27																																																
659	30	SE - Service Elevator Complete	0 d	4/29/27	4/29/27																																																
660		5th Floor	345 d	5/22/26	9/30/27																																																
661		General	345 d	5/22/26	9/30/27																																																
662	20B	5 - Spray Fireproofing - South	10 d	5/22/26	6/5/26																																																
663	MEPF	5 - Overhead MEPF	50 d	7/28/26	10/6/26																																																
664	MEPF	5 - In-Wall MEPF	40 d	8/11/26	10/6/26																																																
665	20B	5 - Spray Fireproofing - North	10 d	8/25/26	9/8/26																																																
666	21	5 - Interior Wall Framing	15 d	9/16/26	10/6/26																																																
667	21	5 - Door Frame Installation	20 d	10/7/26	11/3/26																																																
668	31	5 - Lab Fume Hoods	15 d	10/7/26	10/27/26																																																
669	21	5 - Drywall - 1 Side	10 d	10/7/26	10/20/26																																																
670	20	5 - Blocking & Backing	10 d	10/21/26	11/3/26																																																
671	TCC	5 - In-Wall Inspection/Sign Off	5 d	11/4/26	11/10/26																																																
672	21	5 - Close-In Walls	10 d	11/11/26	11/24/26																																																
673	21	5 - Hang, Tape & Finish Drywall	15 d	11/25/26	12/17/26																																																
674	20B	5 - Spray Fireproofing - Patching	5 d	8/19/27	8/25/27																																																
675	MEPF	5 - Overhead MEPF Inspection	5 d	8/26/27	9/1/27																																																
676	24	5 - Paint Exposed Overhead Ceiling Systems	10 d	9/2/27	9/16/27																																																
677	21	5 - Hardlid Ceiling & Soffit Framing	10 d	9/17/27	9/30/27																																																
678		Finishes	215 d	11/25/26	9/30/27																																																
679	18	5 - Interior Glazing	20 d	11/25/26	12/24/26																																																
680	22	5 - Wall Finishes/Tile	20 d	12/18/26	1/18/27																																																
681	24	5 - Prime/Paint First Coat	15 d	1/19/27	2/8/27																																																
682	31	5 - Millwork/Lab Casework	25 d	2/9/27	3/15/27																																																
683	27	5 - Plumbing Fixtures	25 d	2/23/27	3/29/27																																																
684	24	5 - Sealed Concrete	20 d	3/16/27	4/12/27																																																
685	23	5 - Resilient Tile	10 d	3/16/27	3/29/27																																																



ID	WC	Name	Duration	Start	Finish																								
						O	N	D	2025							2026							2027						
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
686	23	5 - Rubber Flooring - Accent and Sheet	10 d	3/16/27	3/29/27																								
687	23	5 - Carpet Tile	10 d	3/16/27	3/29/27																								
688	23	5 - Luxury Vinyl Tile	10 d	3/16/27	3/29/27																								
689	31	5 - Lab Specialties	30 d	3/16/27	4/26/27																								
690	20	5 - Door Frames/Hardware	30 d	3/30/27	5/10/27																								
691	24	5 - Finish Paint - 2nd Coat	15 d	3/30/27	4/19/27																								
692	31	5 - DIRT Wall Systems	30 d	4/13/27	5/24/27																								
693	MEPF	5 - MEPF Finish Devices	25 d	4/20/27	5/24/27																								
694	20	5 - Corner Guards	5 d	4/20/27	4/26/27																								
695	28	5 - Security/Access Control	20 d	5/11/27	6/8/27																								
696	21	5 - Ceiling Grid/Frame Installation	35 d	5/25/27	7/14/27																								
697	28	5 - Light Fixtures	40 d	6/23/27	8/18/27																								
698	27	5 - Grilles/Diffusers	15 d	7/15/27	8/4/27																								
699	27	5 - Radiant Panel Closures	10 d	7/15/27	7/28/27																								
700	21	5 - Ceiling Tiles - WPC01	20 d	9/2/27	9/30/27																								
701	21	5 - Felt Decorative Acoustic Ceiling Tile - Grid	20 d	9/2/27	9/30/27																								
702	21	5 - Felt Decorative Acoustic Ceiling Tile - Pads	20 d	9/2/27	9/30/27																								
703	TCC	5 - 5th Floor Complete	0 d	9/30/27	9/30/27																								
704		4th Floor	370 d	6/8/26	11/18/27																								
705		General	345 d	6/8/26	10/14/27																								
706	20B	4 - Spray Fireproofing - South	10 d	6/8/26	6/19/26																								
707	MEPF	4 - Overhead MEPF	50 d	8/18/26	10/27/26																								
708	MEPF	4 - In-Wall MEPF	40 d	9/1/26	10/27/26																								
709	20B	4 - Spray Fireproofing - North	10 d	9/9/26	9/22/26																								
710	21	4 - Interior Wall Framing	15 d	10/7/26	10/27/26																								
711	31	4 - Lab Fume Hoods	15 d	10/28/26	11/17/26																								
712	21	4 - Drywall - 1 Side	10 d	10/28/26	11/10/26																								
713	21	4 - Door Frame Installation	20 d	11/4/26	12/3/26																								
714	20	4 - Blocking & Backing	10 d	11/11/26	11/24/26																								
715	TCC	4 - In-Wall Inspection/Sign Off	5 d	11/25/26	12/3/26																								
716	21	4 - Close-In Walls	10 d	12/4/26	12/17/26																								
717	21	4 - Hang, Tape & Finish Drywall	15 d	12/18/26	1/11/27																								
718	20B	4 - Spray Fireproofing - Patching	5 d	8/26/27	9/1/27																								
719	MEPF	4 - Overhead MEPF Inspection	5 d	9/10/27	9/16/27																								
720	24	4 - Paint Exposed Overhead Ceiling Systems	10 d	9/17/27	9/30/27																								
721	21	4 - Hardlid Ceiling & Soffit Framing	10 d	10/1/27	10/14/27																								
722		Finishes	220 d	1/12/27	11/18/27																								
723	22	4 - Wall Finishes/Tile	20 d	1/12/27	2/8/27																								
724	24	4 - Prime/Paint First Coat	15 d	2/9/27	3/1/27																								
725	31	4 - Millwork/Lab Casework	25 d	3/2/27	4/5/27																								
726	27	4 - Plumbing Fixtures	25 d	3/16/27	4/19/27																								
727	31	4 - Lab Specialties	30 d	4/6/27	5/17/27																								
728	24	4 - Sealed Concrete	20 d	4/6/27	5/3/27																								



Wayne State University
Health Sciences Building
Proposal Schedule



ID	WC	Name	Duration	Start	Finish	2025												2026												2027												2028																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
729	23	4 - Resilient Tile	10 d	4/6/27	4/19/27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														



ID	WC	Name	Duration	Start	Finish																												
772	31	3 - Lab Specialties	30 d	4/27/27	6/8/27																												
773	23	3 - Resilient Tile	10 d	4/27/27	5/10/27																												
774	23	3 - Rubber Flooring - Accent and Sheet	10 d	4/27/27	5/10/27																												
775	23	3 - Carpet Tile	10 d	4/27/27	5/10/27																												
776	23	3 - Luxury Vinyl Tile	10 d	4/27/27	5/10/27																												
777	31	3 - DIRT Wall Systems	30 d	5/25/27	7/7/27																												
778	18	3 - Interior Glazing	20 d	5/25/27	6/22/27																												
779	20	3 - Door Frames/Hardware	30 d	6/23/27	8/4/27																												
780	21	3 - Ceiling Grid/Frame Installation	35 d	7/8/27	8/25/27																												
781	28	3 - Light Fixtures	40 d	8/5/27	9/30/27																												
782	28	3 - Security/Access Control	20 d	8/5/27	9/1/27																												
783	27	3 - Grilles/Diffusers	15 d	8/26/27	9/16/27																												
784	27	3 - Radiant Panel Closures	10 d	8/26/27	9/9/27																												
785	21	3 - Ceiling Tiles - WPC01	20 d	9/10/27	10/7/27																												
786	21	3 - Felt Decorative Acoustic Ceiling Tile - Grid	20 d	9/10/27	10/7/27																												
787	21	3 - Felt Decorative Acoustic Ceiling Tile - Pads	20 d	9/10/27	10/7/27																												
788	24	3 - Finish Paint - 2nd Coat	15 d	10/8/27	10/28/27																												
789	MEPF	3 - MEPF Finish Devices	25 d	10/22/27	11/29/27																												
790	20	3 - Corner Guards	5 d	10/29/27	11/4/27																												
791	TCC	3 - 3rd Level Complete	0 d	11/29/27	11/29/27																												
792	2nd Floor		370 d	7/7/26	12/20/27																												
793	General		355 d	7/7/26	11/29/27																												
794	20B	2 - Spray Fireproofing - South	10 d	7/7/26	7/20/26																												
795	MEPF	2 - Overhead MEPF	50 d	9/30/26	12/10/26																												
796	20B	2 - Spray Fireproofing - North	10 d	10/7/26	10/20/26																												
797	MEPF	2 - In-Wall MEPF	40 d	10/21/26	12/17/26																												
798	21	2 - Interior Wall Framing	15 d	11/18/26	12/10/26																												
799	31	2 - Lab Fume Hoods	15 d	12/11/26	1/4/27																												
800	21	2 - Drywall - 1 Side	10 d	12/11/26	12/24/26																												
801	20	2 - Blocking & Backing	10 d	12/28/26	1/11/27																												
802	TCC	2 - In-Wall Inspection/Sign Off	5 d	12/28/26	1/4/27																												
803	21	2 - Door Frame Installation	20 d	1/5/27	2/1/27																												
804	21	2 - Close-In Walls	10 d	1/12/27	1/25/27																												
805	21	2 - Hang, Tape & Finish Drywall	15 d	2/2/27	2/22/27																												
806	20B	2 - Spray Fireproofing - Patching	5 d	10/8/27	10/14/27																												
807	MEPF	2 - Overhead MEPF Inspection	5 d	10/22/27	10/28/27																												
808	24	2 - Paint Exposed Overhead Ceiling Systems	10 d	10/29/27	11/11/27																												
809	21	2 - Hardlid Ceiling & Soffit Framing	10 d	11/12/27	11/29/27																												
810	Finishes		210 d	2/23/27	12/20/27																												
811	22	2 - Wall Finishes/Tile	20 d	2/23/27	3/22/27																												
812	24	2 - Prime/Paint First Coat	15 d	3/23/27	4/12/27																												
813	31	2 - Millwork/Lab Casework	25 d	4/13/27	5/17/27																												
814	27	2 - Plumbing Fixtures	25 d	4/27/27	6/1/27																												

[illegible]



ID	WC	Name	Duration	Start	Finish	2025												2026												2027												2028																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
858	20	1 - Door Frames/Hardware	30 d	6/2/27	7/14/27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		



Wayne State University Health Sciences Building Proposal Schedule



ID	WC	Name	Duration	Start	Finish	2025												2026												2027												2028																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
901	08	SWCF - Top Soil	20 d	11/19/27	12/20/27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
